

REZAYAT GROUP Health and Safety



Initial Incident/Accident Report

Fill the Information Belo	W							
Company: RCL					Da	te: 11/8/2021		
						Time: 09:30		
Location: Jubail								
Project/ Site Name: Berri Gas Plant Aramco					Worst Potential Severity: 4 Actual Severity: 2			
Person(s) Involved:		Employee		Contractor		Others		
1. Robol - 3	99	54	3.					
2. Thuvakaran -	**	ther(s).						
Type of Incident:								
Unknown Now								
Injury Location by Body Parts (Select one or more if necessary):								
Head	T	Chest		Hand		Eyes		
Face		Leg		Arm		Hip		
Neck	1	Abdomen		Wrist		Ankle/Foot		
Back		Stomach		Elbow		Knee	✓	
Nose/ Ears		Shoulder		Fingers/Thumb		Toes		
Type of Injury Sustained (Select one or more if necessary):								
Fracture		Cut/ Laceration	765	Scalping		Bruising		
Loss of Sight		Loss of Consciousness	-	Heat		Amputation		
Dislocation		Crush Injury		Cold	1	Other(s) Sprain		
Abrasion		Suffocation		Burn				
Immediate Cause(s) (Select one or more if necessary):								
				Down / Alaskal Balatad		In a damenta Weibilita		
Safety Rule Violated Lack of Task Skill	1	Lack of Resources Method Deviation	Y	Drugs/ Alcohol Related		Inadequate Visibility	\vdash	
Lack of Supervision	1	Poor Weather Conditions	-	Poor Housekeeping Inadequate Lighting		Employee Morale Employee Attitude	-	
Improper Lifting (MH)	Ė.	Lack of Task Knowledge	_	Poor Team Work	-	Behavior Problem	\vdash	
Not Paying Attention		Lack of Communication	À.	No Risk Assessment		Poor Ground Conditions		
Human Error	1	Incorrect Tools/Equip		Defective Equipment	-	Improper Lifting (crane)		
Inadequate PPE		Defective Tools	1	Unprotected excavation		Unprotected Edge		
Animals		Violence	V	Horseplay		Improper/ Poor Slinging		
Heat Stress		STF Above Ground	1	STF on the Same Level		Manual Handling		
Misuse of Hand Tools		Grinding/Welding		Knives/Sharps		Hit by Vehicle		
Hit by Static Machinery		Heavy Equipment		Splashes from C.P.O.L.		Other(s):		
Stress	-	Fatigue		Vandalism				
Equipment(s) Involved:								
Light Vohiglor		Haarny Vahialos	<u> </u>	Plant Equipment		Ctatic Plant Equipment.		
Light Vehicle:		Heavy Vehicle: Structure:	\rightarrow	Plant Equipment: Scaffold:		Static Plant Equipment: Excavation:		
Building:		structure:	\rightarrow	Scarioid:	-	Excavation:		
Other(s):			-					
Description of the Event:								
During demolition work in 470 area near new ome building three workers were trying to remove the gas alarm lamp stand using by a ladder but while the worker removed the lamp stand the weight of the lamp stand was too heavy than he expected therefore he was not able to balance himself and he slip from the ladder at that time the lamp fell on the other worker who was supporting the ladder on his neck. Although no major injuries happened but swelling was found on the knees of the person who removed the lamp stand and small swelling was also found on the neck of the person who was supporting the ladder. The third person was safe nothing happened to him.								
Immediate Action(s) Taken to Prevent Reoccurrence (If Any):								
 Stop the activity immediately. instructed the supervisor to provide the mobile scaffold and stop using the ladder for the same purpose. Conducted the TBT and share the lesson learned with rest of the site crew. 								
Person Created the Report	:					ARCHITECTURE CONTRACTOR		
		Desition		Cignoture	Y I	Data: 11 /0 /2020		
Name: Sumech Kaimal		Position:		Signature:		Date: 11/9/2020		

Ref:

Version:


RCL-HSE-FM-07.4

INITIAL ACCIDENT AND INCIDENT **NOTIFICATION REPORT**



Rev. Date: June 28, 2021

1.2

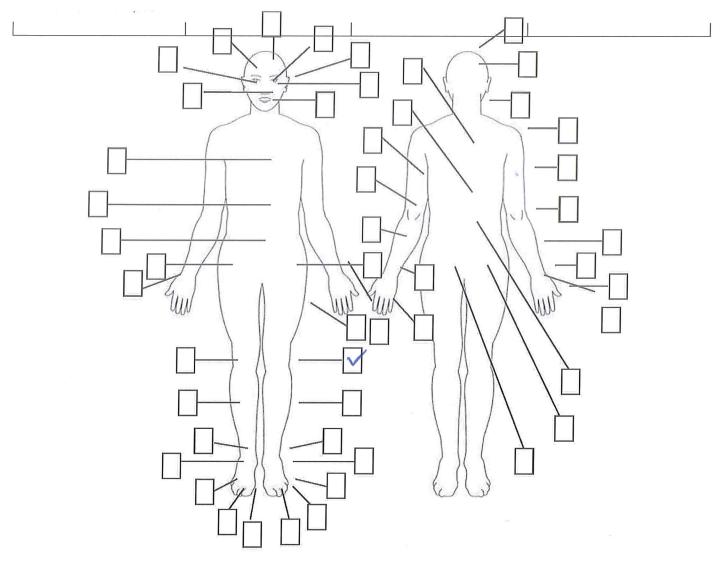

Note: please indicate by using an X in the box next to the injured part/parts, this should match the injury description above.

Ruhul-39954

Signature:

Ref:


RCL-HSE-FM-07.4

INITIAL ACCIDENT AND INCIDENT **NOTIFICATION REPORT**

Version:

1.2

Rev. Date: June 28, 2021

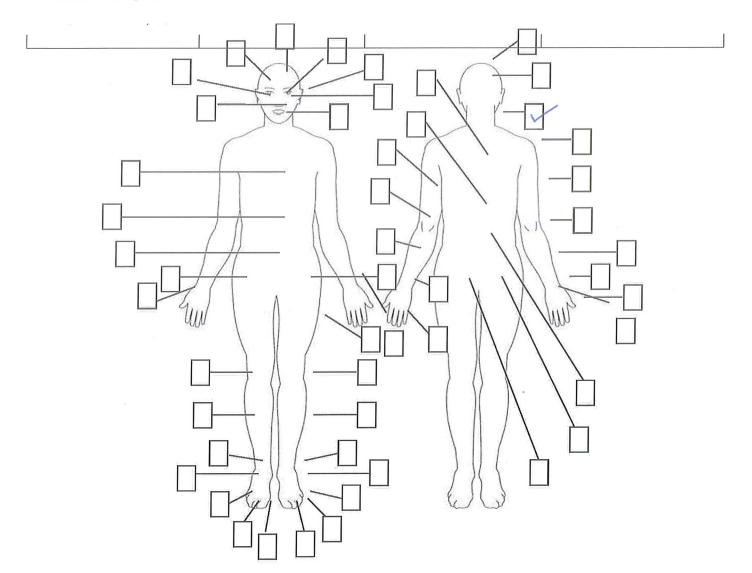

Note: please indicate by using an X in the box next to the injured part/parts, this should match the injury description above.

Name: Thurakaram - 31032932 Signature:
